2-way Conversion Project



Public Works Committee Meeting

August 9, 2022






2-way Conversion Project

- 2018 Bond Funded
- Recommendations identified in the 2015 Downtown Street Study
 - 1. Enhance Vehicular Circulation
 - 2. Promote safe Bicycle and Pedestrian Travel
 - 3. Improve the Downtown Business Environment
- Broken into two sub-projects
 - 1. First and Second Streets
 - 2. Liberty and Main Streets



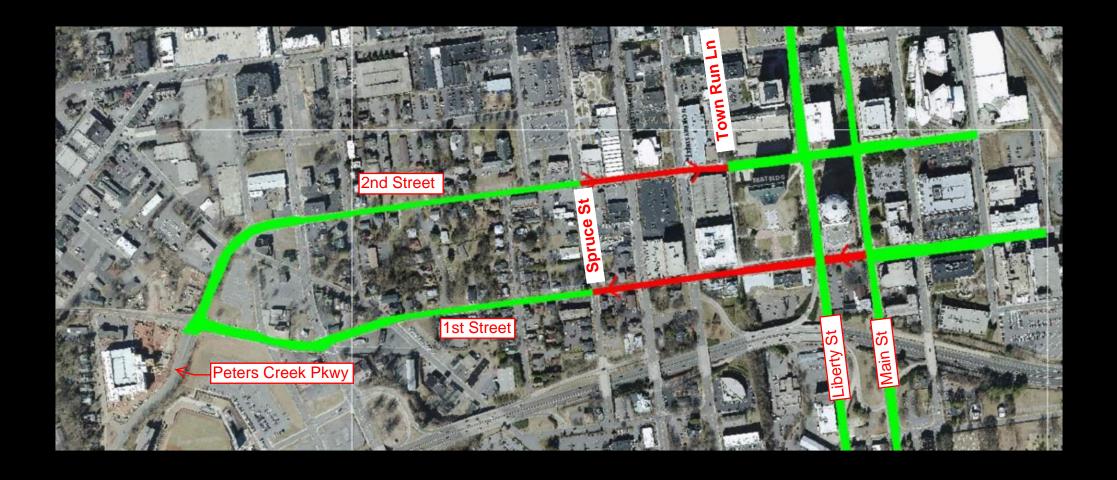

1st Street & 2nd Street

Peters Creek Parkway to Spruce Street



1st Street & 2nd Street

Spruce Street to Chestnut Street



1st Street & 2nd Street

- Current Status
 - Roadway
 - Scheduling 1st St Resurfacing.
 - Contract Negotiations due to Delay
 - Signal Poles (Duke Energy)
 - Work continues on pole foundations.
 - Delays in material procurement have slowed work. Poles are being manufactured and the bolts necessary for the foundations are on order.



1st Street & 2nd Street Cont'd

- Current Schedule
 - Roadway
 - Expected Start Date for Resurfacing: Mid August
 - Work is estimated to take 2-3 months for completion
 - Signal Poles
 - Duke Energy working to having the foundations and poles installed by the end of August-pending anchor bolt availability



Liberty Street & Main Street

Old Salem Road to 2nd Street



Liberty Street & Main Street

2nd Street to Martin Luther King Jr. Drive



Liberty Street & Main Street

- Current Status
 - Working with Duke Energy on mast arm pole design. When design is complete and approved Duke will prepare a service agreement for our review.
 - Coordinating with Duke Energy and other Utility owners on existing utility pole line relocation
 - •Old Salem Rd/Brookstown Ave.
 - Draft relocation agreement received for review.



ONE Way to TWO Way??

Questions???

Questions???

Questions???

Questions???



Questions???

Questions???

Questions???

Questions???

NO Way!!!!!
